

Malta's first offshore wind farm: on schedule?

Testing the Energy Ministry's capacity, bids and timetable against public records

THE CLAIM UNDER REVIEW

“...located beyond Malta's territorial waters... an installed capacity of approximately 300MW...”

“...inform candidates who qualify... by the first part of next year.”

Energy Ministry statement, 22 July 2025 (as reported by TVM News).

Statement as reported; only Minister Dalli's words are in quotation marks in the source.

VERDICT: LARGELY SUPPORTED

Facts hold; the timetable is Off track (pledge)

Version 1.1 · 6 October 2026

Status: draft, pending right of reply

Prepared from public sources and Eurostat data.

Repository: github.com/leandergrech/Mizien

MIŻIEN · AN INDEPENDENT FACT-CHECKING PROJECT

Contest a verdict, with evidence: github.com/leandergrech/Mizien/issues

TL;DR

On 22 July 2025 the Energy Ministry said Malta’s first floating wind farm, of “approximately 300MW”, would be built “beyond Malta’s territorial waters”, that three submissions had been received for the first stage, and that the plan was to inform qualifying candidates of the next phase “by the first part of next year”. We checked the facts against the project’s own documents and Eurostat data, and the timetable against what has been published since.

- 1

The facts hold. InterConnect Malta (ICM), the government company running the process, describes a floating wind farm of around 300 MW beyond the 12-nautical-mile limit, in an area to be declared as Malta’s Exclusive Economic Zone. Three submissions were announced on 22 July 2025, from named applicants.
- 2

The output claim is consistent with national data. ICM says the farm would give up to 0.8 TWh a year, about 25% of Malta’s electricity demand as it stood in 2025. That implies a 30% capacity factor and matches 25% of the 3,252 GWh Eurostat shows Malta supplied in 2025 (production plus imports); it is 27% of final consumption.
- 3

No public sign of the step by the stated time. The “first part of 2026” step, telling qualifying candidates they may continue, has no public notice. ICM’s news list to 3 October 2026 and its tenders page record none. It did issue a EUR 3.6 million metocean survey tender in April 2026, to gather two years of site data for developers.
- 4

What we cannot tell. The notice to candidates may have been sent privately, and the government may have revised the plan without publishing it. MaltaToday reported on 4 August 2025 that the minister, answering a parliamentary question, put the next stage (the invitation to dialogue) at around April 2026 and the contractor’s selection towards the end of 2027 [10]; we found no public notice of that stage either.

THIS CLAIM

SUPPORTED

LARGELY SUPPORTED

NOT SUBSTANTIATED

MISLEADING

CONTRADICTED

≈300 MW

Capacity, beyond 12 nautical miles (ICM, Energy Ministry)

3

Submissions to the first stage, announced 22 Jul 2025

≈25%

Of 2025 electricity supplied would come from the farm (ICM figure; our check 24.6%)

Off track

Pledge label for the “first part of 2026” step, as of 6 Oct 2026

WHAT WOULD MOVE THE VERDICT UP

None for the facts. They rest on the project’s own documents and one national dataset; Supported would need an independent record of the final site and capacity, which will exist only after a concession is awarded.

WHAT WOULD MOVE IT DOWN

A published notice, or a PQQ document, showing that qualifying candidates were informed in the first part of 2026 would move the label to On track or Met. A published revised timetable would reset the baseline. A final contract at a different capacity would change the factual rating.

1

The claim and what we could verify

The Energy Ministry announced the result of the first stage on 22 July 2025. TVM News published the ministry’s statement and a quotation from the Minister, Miriam Dalli [1]; Newsbook published the same announcement [2]. The maintainer supplied the passages (*literature/CC-029/primary-source.md*) and we re-read both pages in full. The ministry’s own page and ICM’s site carry the project description [3, 4]. Only the minister’s words inside quotation marks are quoted; the rest is the ministry statement as the outlet reports it.

Source	What it says	Our access	Status
Energy Ministry statement, as reported by TVM News, 22 Jul 2025 [1]	The wind farm “will be located beyond Malta’s territorial waters”, in an area to be declared part of the EEZ, with “an installed capacity of approximately 300MW”; three submissions; the “current plan is to inform candidates who qualify for the next phase by the first part of next year” (TVM’s rendering of the statement).	Read in full, 6 Oct 2026.	The claim (statement as reported)
Minister Miriam Dalli [1, 2]	“What was once an exploratory initiative has now entered a structured phase” (TVM News [1]). Newsbook [2] reports him describing the announcement as “an important step forward for the project and a clear signal that the process has truly kicked off” (Newsbook’s wording; not quoted elsewhere).	Read in full; Newsbook text checked in an Internet Archive copy of 22 Jul 2025.	Quoted
InterConnect Malta, project page and news, 5 Dec 2024 to 22 Apr 2026 [3, 4, 5, 6]	Around 300 MW; 12 nautical miles or more offshore; up to 0.8 TWh a year; a three-step competitive dialogue (qualification questionnaire, invitation to dialogue, best and final offer); two sites; submissions deadline extended to 21 Jul 2025; a metocean tender of 22 Apr 2026.	Read in full, 6 Oct 2026.	Primary (government company)
Eurostat, nrg_cb_e [7]	Malta electricity production, imports, exports and final consumption, 2019 to 2025.	Downloaded 6 Oct 2026 (data/cc-029/).	Primary data
Trade and press reports [8, 9, 10]	Repeat the timetable; MaltaToday (4 Aug 2025, a parliamentary reply by the minister) says the dialogue stage was planned around April 2026 and the contractor’s selection towards the end of 2027.	Trade pages read; MaltaToday read through an Internet Archive copy of 4 Aug 2025 (the live page returns 403).	Context

WHAT WE COULD NOT READ

The qualification questionnaire documents, the e-tenders notices and any letters to candidates were not available to us (the ministry and ICM’s e-tender portal are browser-only or refused scripted access). The National Energy and Climate Plan’s offshore wind assumption was not read and is not used. Routes tried are in *literature/CC-029/README.md*.

2

Method

Questions. (A) Is the project as described: a floating farm of about 300 MW beyond territorial waters? (B) Were there three first-stage submissions? (C) Is the stated output plausible against national demand? (D) Did the next stage happen when the plan said?

Evidence. For A and B we read the ministry statement and ICM’s own pages. For C we downloaded Malta’s electricity balance from Eurostat (nrg_cb_e, siec E7000, GWh) with *fetch.py* and computed the shares with *calc.py* (*data/cc-029/checks.csv*). The 2025 values carry the Eurostat provisional flag. For D we listed every post ICM published between 1 June 2025 and 6 October 2026 (22 posts, from its website’s public post list), read ICM’s tenders

page, and searched the web for the project's name; the search log is in *literature/CC-029/notes.md*.

The limit of D. Absence of a public notice is not proof that nothing happened: candidates can be told privately. It does show that no progress after the qualification stage has been published, which is what a pledge label judges.

Grades. Official statistics and government project documents are grade C; news and trade reports are grade D and are used to locate what was announced. **Verdicts** and **pledge labels** follow Appendix A.

3 What the evidence shows

The description. ICM's project page says the concession covers design, construction, operation, maintenance and decommissioning of an offshore floating wind farm beyond Malta's 12-nautical-mile territorial waters, with the substation and export cable owned by the government, "around 300MW" delivered to the 132 kV network, "up to 0.8 TWh" a year, under a 35-year agreement with a two-way contract for difference [4]. Two sites are on offer, one of which will be developed [4, 6].

The submissions. The first-stage questionnaire was issued on 5 December 2024 [5]. Its deadline, originally 28 March 2025 ♦, was extended by 115 days to 21 July 2025 after clarification requests [5a]. Three submissions followed: the Code Zero Consortium (led by SEP (Malta) Holding Ltd), Atlas Med Wind (managed by GreenIT SpA, Italy) and MCKEDRIK Sole Member Ltd (Greece) [1, 2]. ICM's December 2024 notice said only the top five candidates would be invited to the next stage [5]; with three submissions, that limit is not a constraint.

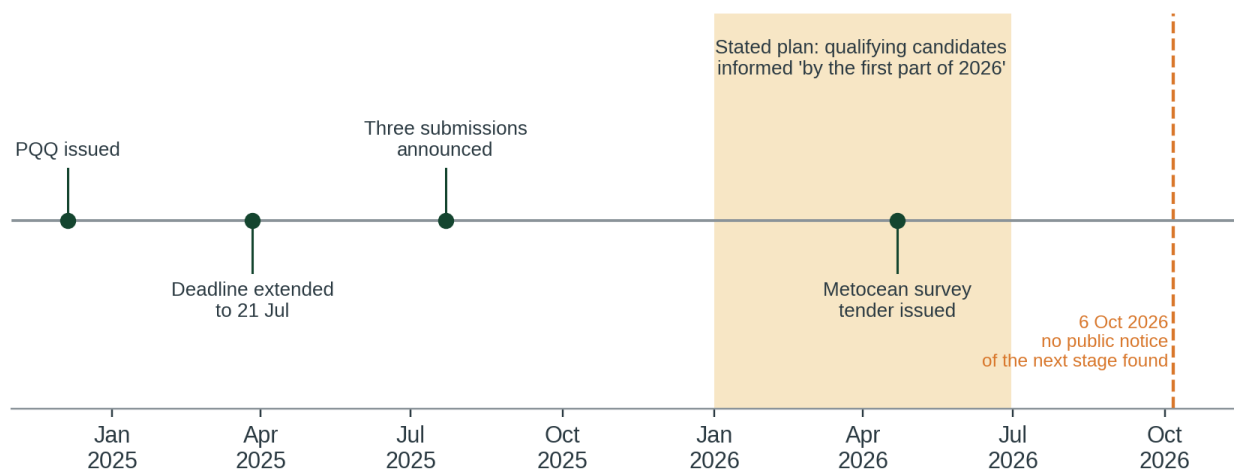


Figure 1. Public milestones of the first offshore wind concession against the timetable stated on 22 July 2025. Sources: ICM news, TVM News, offshoreWIND.biz [1, 5, 6, 9].

The output. 0.8 TWh from 300 MW is a capacity factor of 30.4%, a plausible value for offshore wind. Eurostat gives Malta's 2025 final electricity consumption as 2,970 GWh and electricity supplied (production plus imports minus exports) as 3,252 GWh, 31.7% of it imported by cable [7]. 0.8 TWh is 26.9% of consumption and 24.6% of supply, so ICM's "25% of overall demand as it stood in 2025" [6] matches the supply measure.

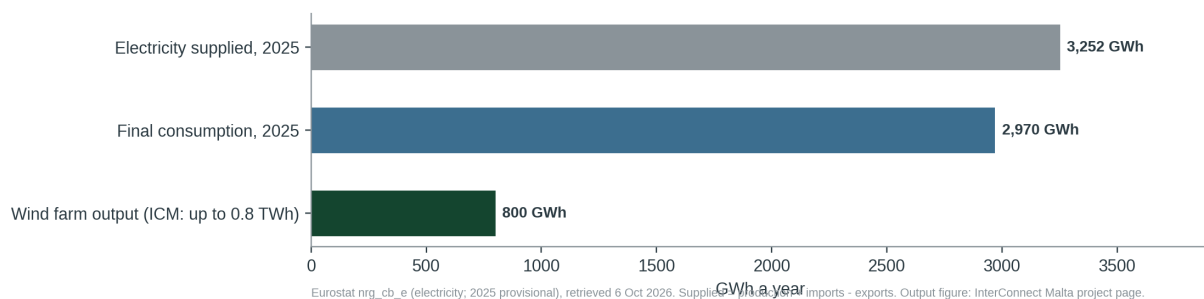


Figure 2. The farm's stated output against Malta's 2025 electricity supply and consumption (Eurostat, 2025 provisional).

The timetable. The 22 July 2025 statement set the plan: tell qualifying candidates “by the first part of next year”, while ICM prepared technical and financial criteria for them [1]. By 6 October 2026, 98 days after the end of June, the end of what we read as “the first part” of 2026, none of ICM’s 22 posts since June 2025, nor its tenders page, records a notice of qualification or of the invitation to dialogue. What ICM did publish, on 22 April 2026, was a EUR 3.6 million tender for two years of metocean measurements at both sites (deadline 21 May 2026), said to let “prospective developers” prepare proposals [6, 9]. That is progress on the project, but it is not the step the plan named.

WHAT THIS DOES AND DOES NOT SHOW

It shows that the project exists as described and that the one public milestone after the questionnaire is a data-collection tender. It does not show the project has failed or that the candidates were not told: the statement concerned an internal evaluation, and a due-diligence step could take longer than planned.

4 Where the evidence points different ways

Has the next stage kept to the stated timetable?		NO PUBLIC SIGN
EVIDENCE OF PROGRESS The project is active: ICM issued the metocean tender in April 2026 and still describes the competitive dialogue structure; the ministry’s plan was a statement of intent, and evaluation of three bulky submissions was said to be thorough [1, 6].	EVIDENCE OF DELAY No public notice of qualification or of the dialogue stage by 6 October 2026, three months after the end of the “first part” of the year. The metocean tender comes with two years of data collection. The minister’s reply reported on 4 August 2025 also put the dialogue stage around April 2026 [10]; no notice of it was found either.	
WHY THEY DIFFER, AND WHAT IT MEANS HERE Both can be true: the work continues, and the stated date was missed in public terms. Only the candidates and ICM know whether the notice was sent. We rate what has been published.		

5 Testing the claim

Sub-claim	Said by	What the evidence shows	Rating
A. A first floating wind farm of about 300 MW, beyond territorial waters	Energy Ministry [1]	ICM’s project page gives the same capacity, floating technology and position beyond 12 nautical miles [4].	ACCURATE
B. Three submissions to the first stage	Energy Ministry [1]	Three named applicants; announced 22 Jul 2025 by the ministry; same in Newsbook and trade media [1, 2, 9].	ACCURATE
C. Output: around a quarter of 2025 demand (ICM)	ICM [6]	0.8 TWh is 24.6% of 2025 electricity supplied and 26.9% of final consumption (Eurostat) [7].	CONSISTENT
D. Qualifying candidates informed “by the first part” of 2026	Energy Ministry [1]	No public notice found by 6 Oct 2026 (ICM posts since June 2025, tenders page); a metocean tender was issued in April 2026; a private notice cannot be excluded.	OFF TRACK (PLEDGE)

6

Verdict, pledge and requests for evidence

VERDICT

LARGELY SUPPORTED

The project, its size and the three submissions are as stated; the timetable is rated as a pledge: Off track. Confidence: moderate.

Why. (1) The factual statements, capacity, position and number of submissions, are confirmed by the government's own project documents and the announcement. (2) The output figure agrees with Eurostat data. (3) We rate *Largely supported* rather than *Supported* because the project is a plan, no concession has been awarded, and the capacity and site may change in the dialogue. (4) The timetable is a plan, not a fact, so it is rated under the pledge scale. Confidence is moderate because the sources are the project's own documents and the timetable rating depends on absence of a notice.

PLEDGE LABEL: OFF TRACK (AS OF 6 OCT 2026)

The step "inform qualifying candidates by the first part of 2026" has no published sign by 6 October 2026, while ICM has published a later data-collection tender. The label is Off track, not Missed, because the evidence that would show it missed (a statement that the step has not happened, or a revised date) was not found, and the notice may have been private. It judges delivery against the pledge as worded, not anyone's intent.

Evidence we are asking for

- ☐ The date candidates were informed of the result of the qualification stage, and how many qualified.
- ☐ A current timetable for the invitation to participate in dialogue and the best and final offer.
- ☐ The e-tenders notice and documents for the metocean survey, and the award, if made.
- ☐ The offshore wind assumption (capacity and year) in Malta's National Energy and Climate Plan, for comparison with 300 MW.

RIGHT OF REPLY

A reply is sought for the pledge label *Off track* (maintainer rule of 5 October 2026). The maintainer handles it; nothing has been sent. Until the deadline has passed this is a draft label on this site only and is not to be circulated elsewhere. The check of ICM's public posts back to June 2025 is complete (see Method); the label is pending right of reply.

7

Limitations

- The ministry's statement is read through TVM News and Newsbook; the ministry's own release was refused to scripts. Only the minister's words are in quotation marks.
- We read no tender documents. Capacity, position and output come from ICM's web pages; the e-tenders portal was not read.
- The Off track label rests on the absence of a public notice, which is weaker evidence than a dated statement. Our reading of "the first part of 2026" as ending on 30 June 2026 is ours; the statement gives no date.
- "The first part of 2026" is not defined in the statement. Reading it more loosely than 30 June 2026 would shorten the gap but not remove it, and the minister's reply of 4 August 2025 [10] placed the dialogue stage around April 2026.
- Eurostat 2025 values are provisional. ICM's 25% is compared with supply and consumption as defined by Eurostat; ICM does not say which measure it used.
- MaltaToday's report [10] was read through an Internet Archive copy of 4 August 2025; the live page was not readable and we did not check whether it has since been edited (its headline and its address differ: "start of 2028")

and “end 2027”).

- The absence of a notice rests on ICM’s public post list and tenders page, the ministry’s release (not readable by scripts) and web searches; a notice on a page we did not read cannot be excluded.

References

- [1] TVM News (22 Jul 2025). Three submissions presented for the first offshore wind farm concession in Malta. <https://tvmnews.mt/en/news/three-submissions-presented-for-the-first-offshore-wind-farm-concession-in-malta/>
- [2] Balzan J. (22 Jul 2025, 17:58). Three firms bid for Malta’s first offshore wind farm concession. Newsbook. <https://newsbook.com.mt/en/three-firms-bid-for-maltas-first-offshore-wind-farm-concession/>
- [3] InterConnect Malta. News and events list (read 6 Oct 2026). <https://icm.mt/news-events/>
- [4] InterConnect Malta. Offshore Renewable Energy Project (read 6 Oct 2026). <https://icm.mt/projects/offshore-renewable-energy-project/>
- [5] InterConnect Malta (5 Dec 2024). Malta launches preliminary qualification questionnaire for offshore floating wind farm project; and (27 Mar 2025) submission deadline extended [5a]. <https://icm.mt/malta-launches-preliminary-qualification-questionnaire-for-offshore-floating-wind-farm-project/>
- [6] InterConnect Malta (22 Apr 2026). Offshore floating wind farm: ICM issues tender to collect data on wind, wave conditions. <https://icm.mt/offshore-floating-wind-farm-icm-issues-tender-to-collect-data-on-wind-wave-conditions/>
- [7] Eurostat. Supply, transformation and consumption of electricity (nrg_cb_e), Malta, retrieved 6 Oct 2026. https://ec.europa.eu/eurostat/databrowser/view/nrg_cb_e/default/table
- [8] offshoreWIND.biz (23 Jul 2025). Three applications submitted in Malta's first offshore wind tender. <https://www.offshorewind.biz/2025/07/23/three-applications-submitted-in-maltas-first-offshore-wind-tender>
- [9] offshoreWIND.biz (21 Apr 2026). Malta opens EUR 3.6 million offshore wind metocean survey tender. <https://www.offshorewind.biz/2026/04/21/malta-opens-eur-3-6-million-offshore-wind-metocean-survey-tender>
- [10] Azzopardi K. (4 Aug 2025). Miriam Dalli: Offshore wind farm contractor to be selected by start of 2028 (title as archived; the address ends “end_2027” and the body says selection “towards the end of 2027”). MaltaToday. Read through the Internet Archive copy of 4 Aug 2025; the live page returns 403. https://web.archive.org/web/20250804160719/https://www.maltatoday.com.mt/news/national/136333/miriam_dalli_offshore_wind_farm_contractor_to_be_selected_by_end_2027
- [11] Mizien. Calculation script and outputs: tools/cc-029-report/calc.py; data/cc-029/checks.csv.

Appendix A: series standards and verdict scale

Every investigation in this series follows the same rules so that verdicts are comparable and challengeable.

Verdict	Meaning
SUPPORTED	Evidence consistently backs the claim as stated.
LARGELY SUPPORTED	Backed by the evidence, with minor caveats that do not change the substance.
NOT SUBSTANTIATED	Stated more strongly than the evidence offered or available allows. May be true in some conditions but has not been shown.
MISLEADING	Omits material facts so that the overall impression is inaccurate, even if individual statements are defensible.
CONTRADICTED	The available evidence points against the claim.

Pledge labels

A pledge is a promise of future action, so it cannot be true or false when it is made. It gets one of these labels instead of a verdict, with the date of the evidence behind it.

Pledge label	Meaning
NOT MEASURABLE	The pledge as worded has no definition, baseline or date against which delivery could be checked.
NOT YET DUE	Measurable; the deadline or term has not passed and no progress data have been published yet.
ON TRACK	Published progress is at or ahead of a straight-line path (or the pledge's own milestones) to the target by the deadline.
OFF TRACK	Published progress is behind that path, and the target has not yet been shown to be met or missed.
MET	Documents or data show the target was reached, by the deadline if one was set.
MISSED	The deadline or term has passed, and documents or data that can be shown say the target was not reached.

Confidence

High: multiple independent lines of evidence agree. **Moderate:** evidence is relevant but incomplete or indirect. **Low:** evidence is thin, second-hand or conflicting.

Evidence grades

A experiment · B observational study with a control or gradient · C review, guidance or official statistics · D assertion or anecdote. ♦ marks a source known only second-hand.

Standards

- **Quote the speaker, not the headline**, with outlet and date, and link the original where possible.
- **Separate the claim from the evidence offered for it**, and say who made which statement.
- **Grade the evidence** and show differing views side by side where the evidence is unsettled.
- **State what we could not access or verify**, and what would change the verdict either way.
- **Ask for the missing evidence** in specific, answerable requests.

- **Offer a right of reply** where a check finds a claim Not substantiated, Misleading or Contradicted (or a pledge Not measurable, Off track or Missed), before wider circulation, and append responses.
- **Correct errors openly** with a version number and change log.
- **Whistle-blow only on evidence:** a verdict of *Misleading* or *Contradicted* requires documents or data that can be shown, not inference.
- **Check every side.** Government, opposition, NGOs and developers are held to the same standard.

Appendix B: revision log

Version	Date	Change
1.0	6 Oct 2026	First issue. Verdict Largely supported (moderate confidence); pledge label Off track; pending right of reply.
1.1	6 Oct 2026	Corrections after audit: MaltaToday report now read (Internet Archive copy) and cited with its exact title; ICM post list checked back to June 2025 (22 posts) and the absence statement limited to what was searched; TL;DR wording softened; Newsbook quotation checked and attributed to Newsbook; flyer inference removed. Verdict and label unchanged; pending right of reply.
